



Resources
Regulator

FWP0001781

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

Saturday 1 November 2025 to Tuesday 31 October 2028

Summary

| Detail | |
|---|---|
| Mine | Donaldson Open Cut Coal Mine |
| Reference | FWP0001781 |
| Forward program commencement date | Saturday 1 November 2025 |
| Forward program end date | Tuesday 31 October 2028 |
| Forward program revision (if applicable) | |
| Contact | Steven Vickers |
| Mining leases | ML 1461 (1992) |
| Project location | Bloomfield Collieries Pty Ltd |
| Date of submission | Friday 30 January 2026 |
| Document URL | https://www.bloomcoll.com.au/sustainability/environmental-management/donaldson-abel-mine |

Security reminder: Please exercise caution before opening external links. If a link appears suspicious, avoid clicking it and report it to the Resources Regulator.

Important

The department may make the information in your program and any supporting information available for inspection by members of the public, including by publication on its website or by displaying the information at any of its offices. If you consider any part of your program to be confidential, please communicate this to the department via the message function on this submission within the Resources Regulator Portal.

Three-year forecast - surface disturbance activities

Project description

The Donaldson Mine was acquired by the Bloomfield Group in 2025. The Bloomfield Group also owns and operates the Abel Underground Coal Mine, with surface facilities partly integrated with the Donaldson Mine Site and underground mining operations occurring immediately south of the Donaldson Mine Site. Development consents DA 98/01173 and DA 118/698/22 for the Donaldson Mine were granted in December 1999. Development commenced January 2001 and the first coal was dispatched during March 2001. Consent for mining operations lapsed on 31 December 2013, however, certain conditions, including rehabilitation requirements, continue to apply without a specified approval lapse date.

Description of surface disturbance activities

Exploration activities

No surface exploration activities are anticipated to be required or to occur within the Donaldson Mine Site in the next three years

Construction activities

No construction activities are anticipated to be required or to occur within the Donaldson Mine Site in the next three years.

Mining schedule

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

Mining development method and sequencing and general mine features.

As the Donaldson Mine is under care and maintenance, no mining operations are currently planned in the next three years. During care and maintenance, the remaining 'operational' areas of the Donaldson Mine will not be available for rehabilitation prior to closure of the Abel Mine. As such, opportunities for further progressive rehabilitation are limited.

Areas identified for emplacements, the sequencing of emplacements, construction, and management.

As the Donaldson Mine is under care and maintenance, no mining operations are currently planned in the next three years.

Processing infrastructure activities and the location of tailings facilities and schedule for emplacement.

As the Donaldson Mine is under care and maintenance, no mining operations are currently planned in the next three years.

Waste disposal and materials handling operations.

As the Donaldson Mine is under care and maintenance and administrative / maintenance activities are undertaken within the Abel Underground Mine area, no specific waste disposal or handling is currently planned in the next 3 years for the Donaldson Mine.

Key production milestones

| MATERIAL | UNIT | YEAR 1 | YEAR 2 | YEAR 3 |
|-------------------------------------|-------------------|--------|--------|--------|
| Stripped topsoil (if applicable) | (m ³) | 0 | 0 | 0 |
| Rock/overburden | (m ³) | 0 | 0 | 0 |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| | | | | |
|------------------------------|------|---|---|---|
| Ore | (Mt) | 0 | 0 | 0 |
| Reject material ¹ | (Mt) | 0 | 0 | 0 |
| Product | (Mt) | 0 | 0 | 0 |

¹This includes coarse rejects, tailings and any other wastes resulting from beneficiation.

Three-year rehabilitation forecast

Rehabilitation planning schedule

Rehabilitation planning schedule

Continued rehabilitation and environmental monitoring will be undertaken which will provide further information for mine closure planning. Prior to mine closure additional closure planning, including completion of a rehabilitation materials balance report (for capping material and growth medium), updated water modelling, and final void design, will be undertaken for the West and Square Pits.

Stakeholder consultation

No specific stakeholder consultation is currently planned during the next 3 years. Consultation will occur within the next three years with various stakeholders regarding further mine closure activities.

Rehabilitation studies, risk assessments and/or design work

A risk assessment to address the risks associated with rehabilitation of the Donaldson Mine was developed in conjunction with the preparation of the Rehabilitation Management Plan (RMP) for the Donaldson Mine by Yancoal. A summary of the risk assessment is available in the RMP. The risk assessment will be reviewed and updated in 2026 and whenever any risk control measures are updated, or any foreseeable hazard that presents a risk to achieving the rehabilitation objectives outlined in the RMP is identified. As part of the rehabilitation materials balance report, conceptual final landform design / cut and fill calculations will be undertaken to inform the materials balance and updated water modelling may be completed within the next three years.

Rehabilitation research and trials

| RRT NUMBER | PROJECT/TRIAL NAME | OBJECTIVE OF TRIAL/PROJECT | METHODOLOGY | EXPECTED DATE OF COMPLETION | STATUS |
|---------------|--------------------|----------------------------|-------------|--------------------------------|--------|
| | | | | | |

Rehabilitation maintenance and corrective actions

No rehabilitation performance issues (beyond ongoing weed control), or knowledge gaps have been identified to date. As such, no specific rehabilitation maintenance or corrective actions have been identified. Notwithstanding, rehabilitation monitoring will continue to measure the performance of previously rehabilitated areas of the Donaldson Mine Site. In addition, ongoing maintenance activities including weed and pest control programs will also be undertaken. Rehabilitation monitoring will focus upon determining whether progress towards achieving the relevant performance indicators and completion and relinquishment criteria presented in Section 4.1 of the RMP are being achieved. The RMP also presents the proposed rehabilitation monitoring methodology for each indicator and criteria identified. In addition to other environmental monitoring, an annual rehabilitation review will be undertaken for rehabilitation areas to assess the progress of rehabilitation and need for remedial measures. Rehabilitation monitoring plots have been established within previously rehabilitated areas to assess and record progress towards the completion criteria outlined in the RMP. Additional plots will also be established following the establishment of additional areas of rehabilitation.

Rehabilitation schedule

As the Donaldson Mine is under care and maintenance, no mining operations or rehabilitation is currently planned in the next three years. The Bloomfield Group are currently reviewing the rehabilitation requirements for the West and Square Pits and propose to explore opportunities to optimise the final landform to support the final landuse.

Completion of rehabilitation

It is not anticipated that an application for rehabilitation completion will be lodged in the next three years.

Subsidence remediation for underground operations

No areas affected by subsidence are located within the Donaldson Mine Site.

Progressive mining and rehabilitation statistics

Three-yearly forecast cumulative disturbance and rehabilitation progression

| Forecast | | UNIT | YEAR 1 | YEAR 2 | YEAR 3 |
|----------|--|------|--------|--------|--------|
| A1 | Total disturbance footprint - surface disturbance | (ha) | 303.12 | 303.12 | 303.12 |
| O | Total active disturbance | (ha) | 82.76 | 82.76 | 82.76 |
| P | Total new area of land proposed for active rehabilitation | (ha) | 0 | 0 | 0 |

Rehabilitation key performance indicators (KPIs)

| | Forecast | UNIT | YEAR 1 | YEAR 2 | YEAR 3 |
|---|---|-------------|---------------|---------------|---------------|
| O | Total new disturbance area during reporting period | (ha) | | | |
| P | Total new area of land proposed for rehabilitation during the reporting period | (ha) | | | |
| Q | Annual rehabilitation to disturbance ratio | | | | |

Attachment 1 - Reporting Definitions

| REPORTING CATEGORY | DEFINITION |
|--|--|
| A Total disturbance footprint - surface disturbance | <p>All areas within a mining lease that either have at some point in time or continue to pose a rehabilitation liability due to surface disturbance activities.</p> <p>The total disturbance footprint is the sum of the total active disturbance, decommissioning, landform establishment, growth medium development, ecosystem and land use establishment, ecosystem and land use development and rehabilitation completion (see definitions below).</p> <p>Underground mining operations should not include the footprint of underground mining areas/subsidence management areas in the total disturbance footprint.</p> |
| B Total active disturbance | <p>Includes on-lease exploration areas, stripped areas ahead of mining, infrastructure areas, water management infrastructure, sewage treatment facilities, topsoil stockpile areas, access tracks and haul roads, active mining areas, waste rock emplacements (active/unshaped/in or out-of-pit), tailings dams (active/unshaped/uncapped) and temporary stabilised areas (e.g. areas sown with temporary cover crops for dust mitigation and temporary rehabilitation).</p> |
| C Rehabilitation - land preparation | <p>Includes the sum of all disturbed land within a mining lease that have commenced</p> |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| REPORTING CATEGORY | DEFINITION |
|--------------------|---|
| | <p>any, or all, of the following phases of rehabilitation - decommissioning, landform establishment and growth medium development.</p> <p>Refer to the glossary of terms in this document for the definition of these phases of rehabilitation.</p> |
| D | <p>Ecosystem and land use establishment</p> <p>Includes the area which has been seeded/planted with the target vegetation species for the intended final land use. However, vegetation has not matured to a stage where it can be demonstrated that it will be sustainable for the long term and or require only a maintenance regime consistent with target reference/analogue sites.</p> <p>Typically, rehabilitation areas would be in this phase for at least two years (and usually more) before rehabilitation can be classified as being in the ecosystem and land use development phase. This phase does not apply to infrastructure areas that are being retained as part of final land use for the site.</p> |
| O | <p>The area of any new active disturbance that will be created during the next three years, as defined under definition A1 (definition A1 Table 5).</p> |
| P | <p>The sum of any new rehabilitation to be commenced in the next three years. These areas may be in the phases "Rehabilitation - Land Preparation" or the "Ecosystem & Land Use Establishment" (definitions C & D in Table 5).</p> |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| REPORTING CATEGORY | DEFINITION |
|--------------------|---|
| Q | The rehabilitation to disturbance ratio (S / R) indicates how many hectares of new rehabilitation are undertaken for each hectare of land disturbed during the three years. A ratio of 1/1 indicates that the area of new rehabilitation and disturbance in that period are the same. |

Attachment 2 - Definitions

| WORD | DEFINITION |
|---|---|
| Active | In the context of rehabilitation, land associated with mining domains is considered 'active' for the period following disturbance until the commencement of rehabilitation. |
| Active mining phase of rehabilitation | In the context of rehabilitation, the active mining phase of rehabilitation constitutes the rehabilitation activities undertaken during mining operations such as salvaging and managing soil resources, salvaging habitat resources, and native seed collection. This phase also includes management actions taken during operations to manage risks to rehabilitation and enhance rehabilitation outcomes such as selective handling of waste rock and management of tailings emplacements. |
| Analogue site | In the context of rehabilitation, an analogue site is a 'reference site' that represents an example of the defining characteristics (such as vegetation composition and structure or agricultural productivity) of the final land use. Characteristics of analogue sites can be assessed to develop the rehabilitation objectives and completion criteria for final land use domains. |
| Annual rehabilitation report and forward program | As described in the Mining Regulation 2016. |
| Annual reporting period | As defined in the Mining Regulation 2016. |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|--|--|
| Closure | A whole-of-mine-life process, which typically culminates in the relinquishment of the mining lease. It includes decommissioning and rehabilitation to achieve the approved final land use(s). |
| Decommissioning | The process of removing mining infrastructure and removing contaminants and hazardous materials. |
| Decommissioning Phase of Rehabilitation | Activities associated with the removal of mining infrastructure and removal and/or remediation of contaminants and hazardous materials. In the context of the rehabilitation management plan this phase of rehabilitation may also include studies and assessments associated with decommissioning and demolition of infrastructure or works carried out to make safe or 'fit for purpose' built infrastructure to be retained for future use(s) following lease relinquishment. |
| Department | Department of Primary Industries and Regional Development. |
| Disturbance | See Surface Disturbance. |
| Disturbance area | An area that has been disturbed and that requires rehabilitation. This may include areas such as on-licence exploration areas, stripped areas ahead of mining, infrastructure areas, water management infrastructure, sewage treatment facilities, topsoil stockpile areas, access tracks and haul roads, active mining areas, waste emplacements (active/unshaped/in or out-of-pit), tailings dams (active/unshaped/uncapped), and areas requiring rehabilitation that are temporarily stabilised (i.e. managed to minimise dust generation and/or erosion). |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|---|---|
| Domain | An area (or areas) of the land that has been disturbed by mining and has a specific operational use (mining domain) or specific final land use (final land use domain). Land within a domain typically has similar geochemical and/or geophysical characteristics and therefore requires specific rehabilitation activities to achieve the associated final land use. |
| Ecosystem and Land Use Development | <p>This phase of rehabilitation consists of the activities to manage maturing rehabilitation areas on a trajectory to achieving the approved rehabilitation objectives and completion criteria.</p> <p>For vegetated land uses this phase may include processes to develop characteristics of functional self-sustaining ecosystems, such as nutrient recycling, vegetation flowering and reproduction, and increasing habitat complexity, and development of a productive, self-sustaining soil profile.</p> <p>This phase of rehabilitation may include specific vegetation management strategies and maintenance such as tree thinning, supplementary plantings and weed management.</p> |
| Ecosystem and Land Use Establishment | <p>This phase of rehabilitation consists of the processes to establish the approved final land use following construction of the final landform.</p> <p>For vegetated land uses this rehabilitation phase includes establishing the desired vegetation community and implementing land management activities such as weed control. This phase of rehabilitation may also include habitat augmentation such as installation of nest boxes.</p> |
| Exploration | Has the same meaning as that term under the State Environmental Planning Policy (Mining, |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|---|--|
| | Petroleum Production and Extractive Industries) 2007. |
| Final landform and rehabilitation plan | As defined in the Mining Regulation 2016. |
| Final land use | As defined in the Mining Regulation 2016. |
| Form and way | Means the form and way approved by the Secretary. Approved form and way documents are available on the department's website. |
| Growth Medium Development | <p>This phase of rehabilitation consists of activities required to establish the physical, chemical and biological components of the substrate required to establish the desired vegetation community (including short lived pioneer species).</p> <p>This phase may include spreading the prepared landform with topsoil and/or subsoil and/or soil substitutes, applying soil ameliorants to enhance the physical, chemical and biological characteristics of the growth media, and actions to minimise loss of growth media due to erosion.</p> |
| Habitat | Has the same meaning as that term under the Biodiversity Conservation Act 2016 and the Fisheries Management Act 1994 (as relevant). |
| Indicator | An attribute of the biophysical environment (e.g. pH, topsoil depth, biomass) that can be used to approximate the progression of a biophysical process. It can be measured and audited to demonstrate (and track) the progress of an aspect of rehabilitation towards a desired completion |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|-----------------------------------|---|
| | criterion (i.e. defined end point). It may be aligned to an established protocol and used to evaluate changes in a system. |
| Land | As defined in the Mining Act 1992. |
| Landform Establishment | <p>This phase of rehabilitation consists of the processes and activities required to construct the final landform.</p> <p>In addition to profiling the surface of rehabilitation areas to the approved final landform profile this phase may include works to construct surface water drainage features, encapsulate problematic materials such as tailings, and prepare a substrate with the desired physical and chemical characteristics (e.g. rock raking or ameliorating sodic materials).</p> |
| Large mine | As defined in the Mining Regulation 2016. |
| Lease holder | The holder of a mining lease. |
| Life of mine | The timeframe of how long a mine is approved to mine, from commencement to closure. |
| Mine rehabilitation portal | Means the Resources Regulator's online portal that lease holders must use (via a registered account) to: |

| WORD | DEFINITION |
|------------------------------|---|
| | <ul style="list-style-type: none">• upload rehabilitation geographical information system (GIS) spatial data• develop rehabilitation GIS spatial data (using online tracing functions)• generate rehabilitation plans and rehabilitation statistics using the map viewer and Rehabilitation Key Performance Indicator functionalities. <p>Data submitted to the mine rehabilitation portal is collated in a centralised geodatabase for use by the Resources Regulator to regulate rehabilitation performance of lease holders.</p> |
| Mining area | As defined in the Mining Act 1992. |
| Mining domain | A land management unit with a discrete operational function (e.g. overburden emplacement), and therefore similar geophysical characteristics, that will require specific rehabilitation treatments to achieve the final land use(s). |
| Mining land | As defined in the Mining Act 1992. |
| Native vegetation | Has the same meaning as that term under section 60B of the Local Land Services Act 2013. |
| Overburden | Material overlying coal or a mineral deposit. |
| Performance indicator | An attribute of the biophysical environment (for example pH, slope, topsoil depth, biomass) that can be used to demonstrate achievement of a rehabilitation objective. It can be measured and audited to |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|-----------------------------------|--|
| | demonstrate (and track) the progress of an aspect of rehabilitation towards a desired completion criterion, that is, a defined end point. It may be aligned to an established protocol and used to evaluate changes in a system. |
| Phases of rehabilitation | The stages and sequences of actions required to rehabilitate disturbed land to achieve the final land use. The phases of rehabilitation are: <ul style="list-style-type: none">• active mining• decommissioning• landform Establishment• growth medium development• landform Establishment• ecosystem and land use establishment• ecosystem and land use development |
| Progressive rehabilitation | The progress of rehabilitation towards achieving the approved rehabilitation completion criteria. This may be described in terms of domains, phases, performance indicators and rehabilitation completion criteria. |
| Rehabilitation Completion | The final phase of rehabilitation when a rehabilitation area has achieved the approved rehabilitation objectives and rehabilitation completion criteria for the final land use. Rehabilitation areas may be classified as complete when the Resources Regulator has determined in writing that the relevant |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|---|---|
| | rehabilitation obligations have been fulfilled following submission of <i>Form ESF2 Rehabilitation completion and/or review of rehabilitation cost estimate application</i> by the lease holder. |
| Rehabilitation Completion criteria | As defined in the Mining Regulation 2016. |
| Rehabilitation cost estimate | As defined in the Mining Regulation 2016. |
| Rehabilitation management plan | As defined in the Mining Regulation 2016. |
| Rehabilitation objectives | As defined in the Mining Regulation 2016. |
| Rehabilitation risk assessment | As defined in the Mining Regulation 2016. |
| Rehabilitation schedule | The defined timeframes for progressive rehabilitation set out in the forward program. |
| Relevant stakeholders | Means any persons or bodies who may be affected by the mining operations, including rehabilitation, carried out on the lease land, and includes: <ul style="list-style-type: none">• the relevant development consent authority• the local council• the relevant landholder(s)• community consultative committee (if required under the development consent) or equivalent |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|----------------------------|---|
| | <p>consultative group</p> <ul style="list-style-type: none">• affected land holder(s)• government agencies relevant to the final land use• affected infrastructure authorities (electricity, telecommunications, water, pipeline, road, rail authorities)• local Aboriginal communities, and• any other person or body determined by the Minister to be a relevant stakeholder in relation to a mining lease. |
| Risk | The effect of uncertainty on objectives. It is measured in terms of consequences and likelihood (AS/NZS ISO 31000:2009). |
| Secretary | The Secretary of the department. |
| Security deposit | An amount that a mining lease holder is required to provide and maintain under a mining lease condition, to secure funding for the fulfilment of obligations under the lease (including obligations that may arise in the future). |
| Surface disturbance | Includes activities that disturb the surface of the mining area, including mining operations, ancillary mining activities and exploration. |

DONALDSON OPEN CUT COAL MINE FORWARD PROGRAM

FWP0001781 | Saturday 1 November 2025 to Tuesday 31 October 2028

Resources Regulator

| WORD | DEFINITION |
|-----------------|---|
| Tailings | A combination of the fine-grained solid material remaining after the recoverable metals and minerals have been extracted from the mined ore, and any process water ² . |
| Waste | Has the same meaning as that term under the <i>Protection of the Environment Operations Act 1997</i> . |

²Commonwealth of Australia (DITR), 2007. Tailings Management.


Attachment 3 - Plans

Plan 2A attachment not provided.

Plan 2B attachment not provided.

Plan 2C attachment not provided.

Donaldson Open Cut Coal Mine Plan 2A Mining and Rehabilitation – Year 1

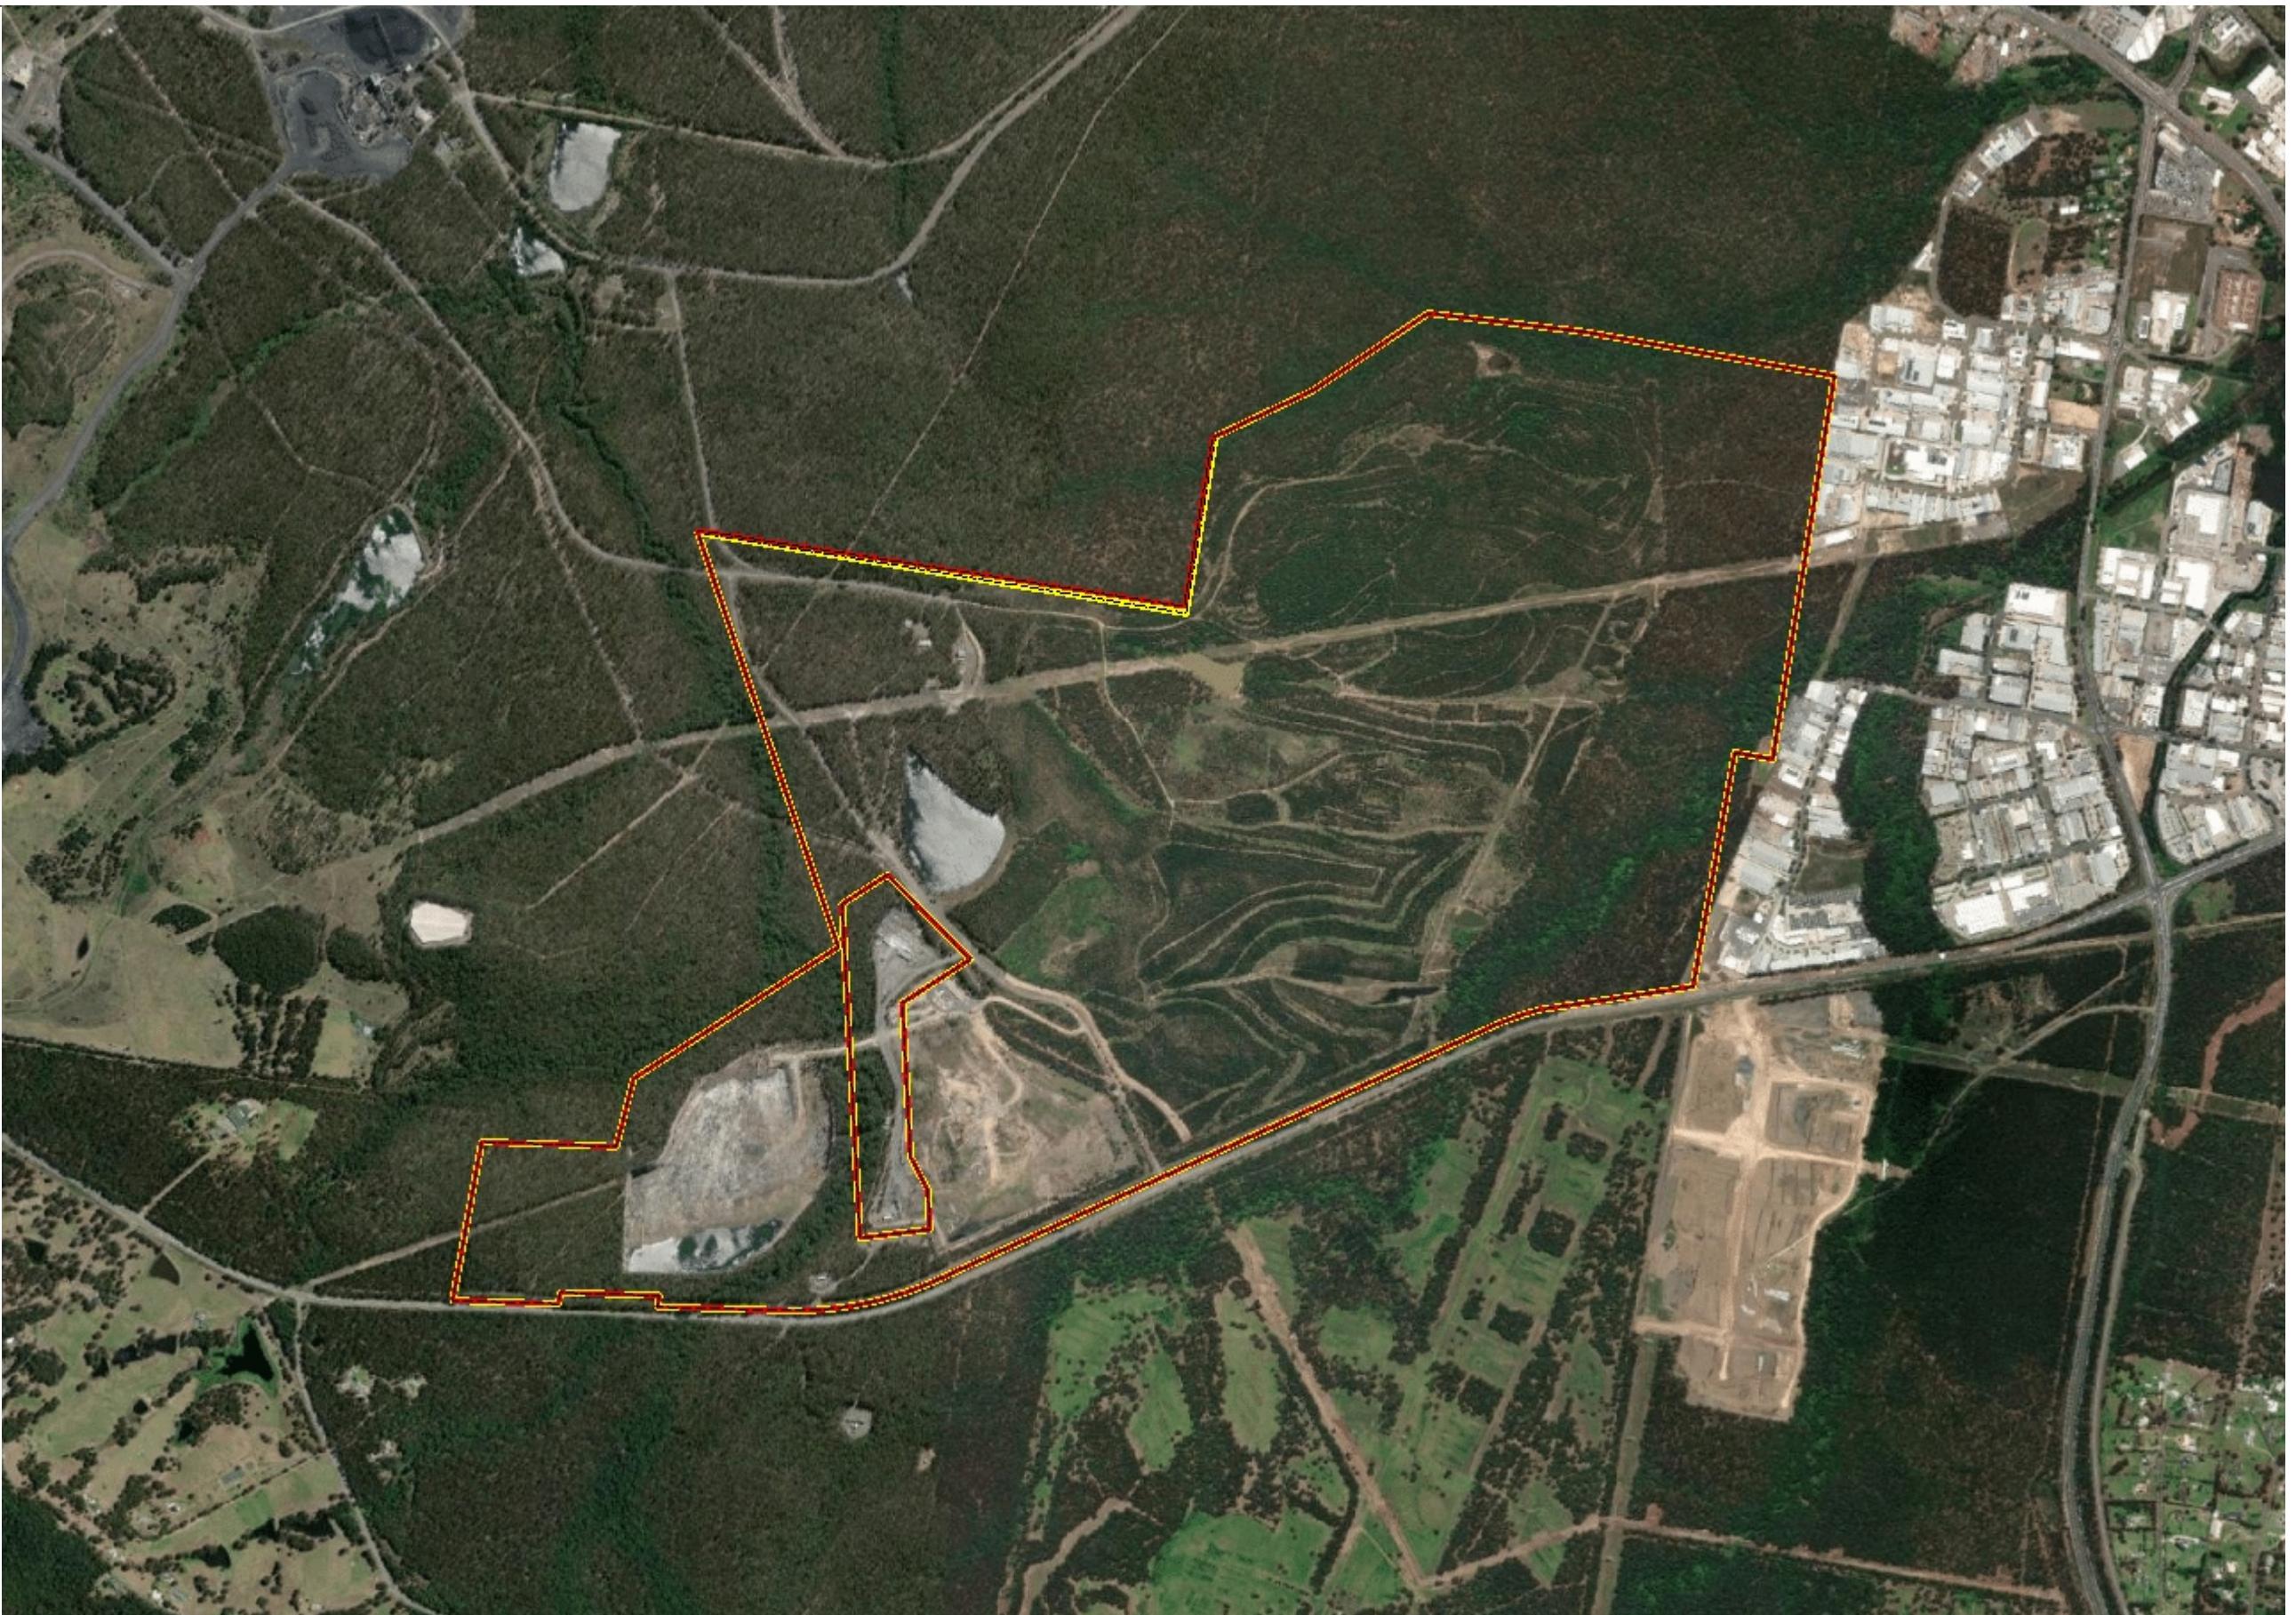

Legend

- Forecast Data Year1
 - Forecast Disturbance
 - Forecast Land Prepared for Rehabilitation
 - Ecosystem and Land Use Establishment
- Project Approval Boundary
- Mine Operations Area
- World Imagery
- Low Resolution 15m Imagery
- High Resolution 60cm Imagery
- High Resolution 30cm Imagery
- Citations

Notes

30/1/26
Submission ID number 11342


1,086.3 0 543.15 1,086.3 Meters

WGS_1984_Web_Mercator_Auxiliary_Sphere
© DRE

This map is a user generated static output from an Internet mapping site and is for reference only. Data layers that appear on this map may or may not be accurate, current, or otherwise reliable.

THIS MAP IS NOT TO BE USED FOR NAVIGATION

Donaldson Open Cut Coal Mine Plan 2B Mining and Rehabilitation – Year 2

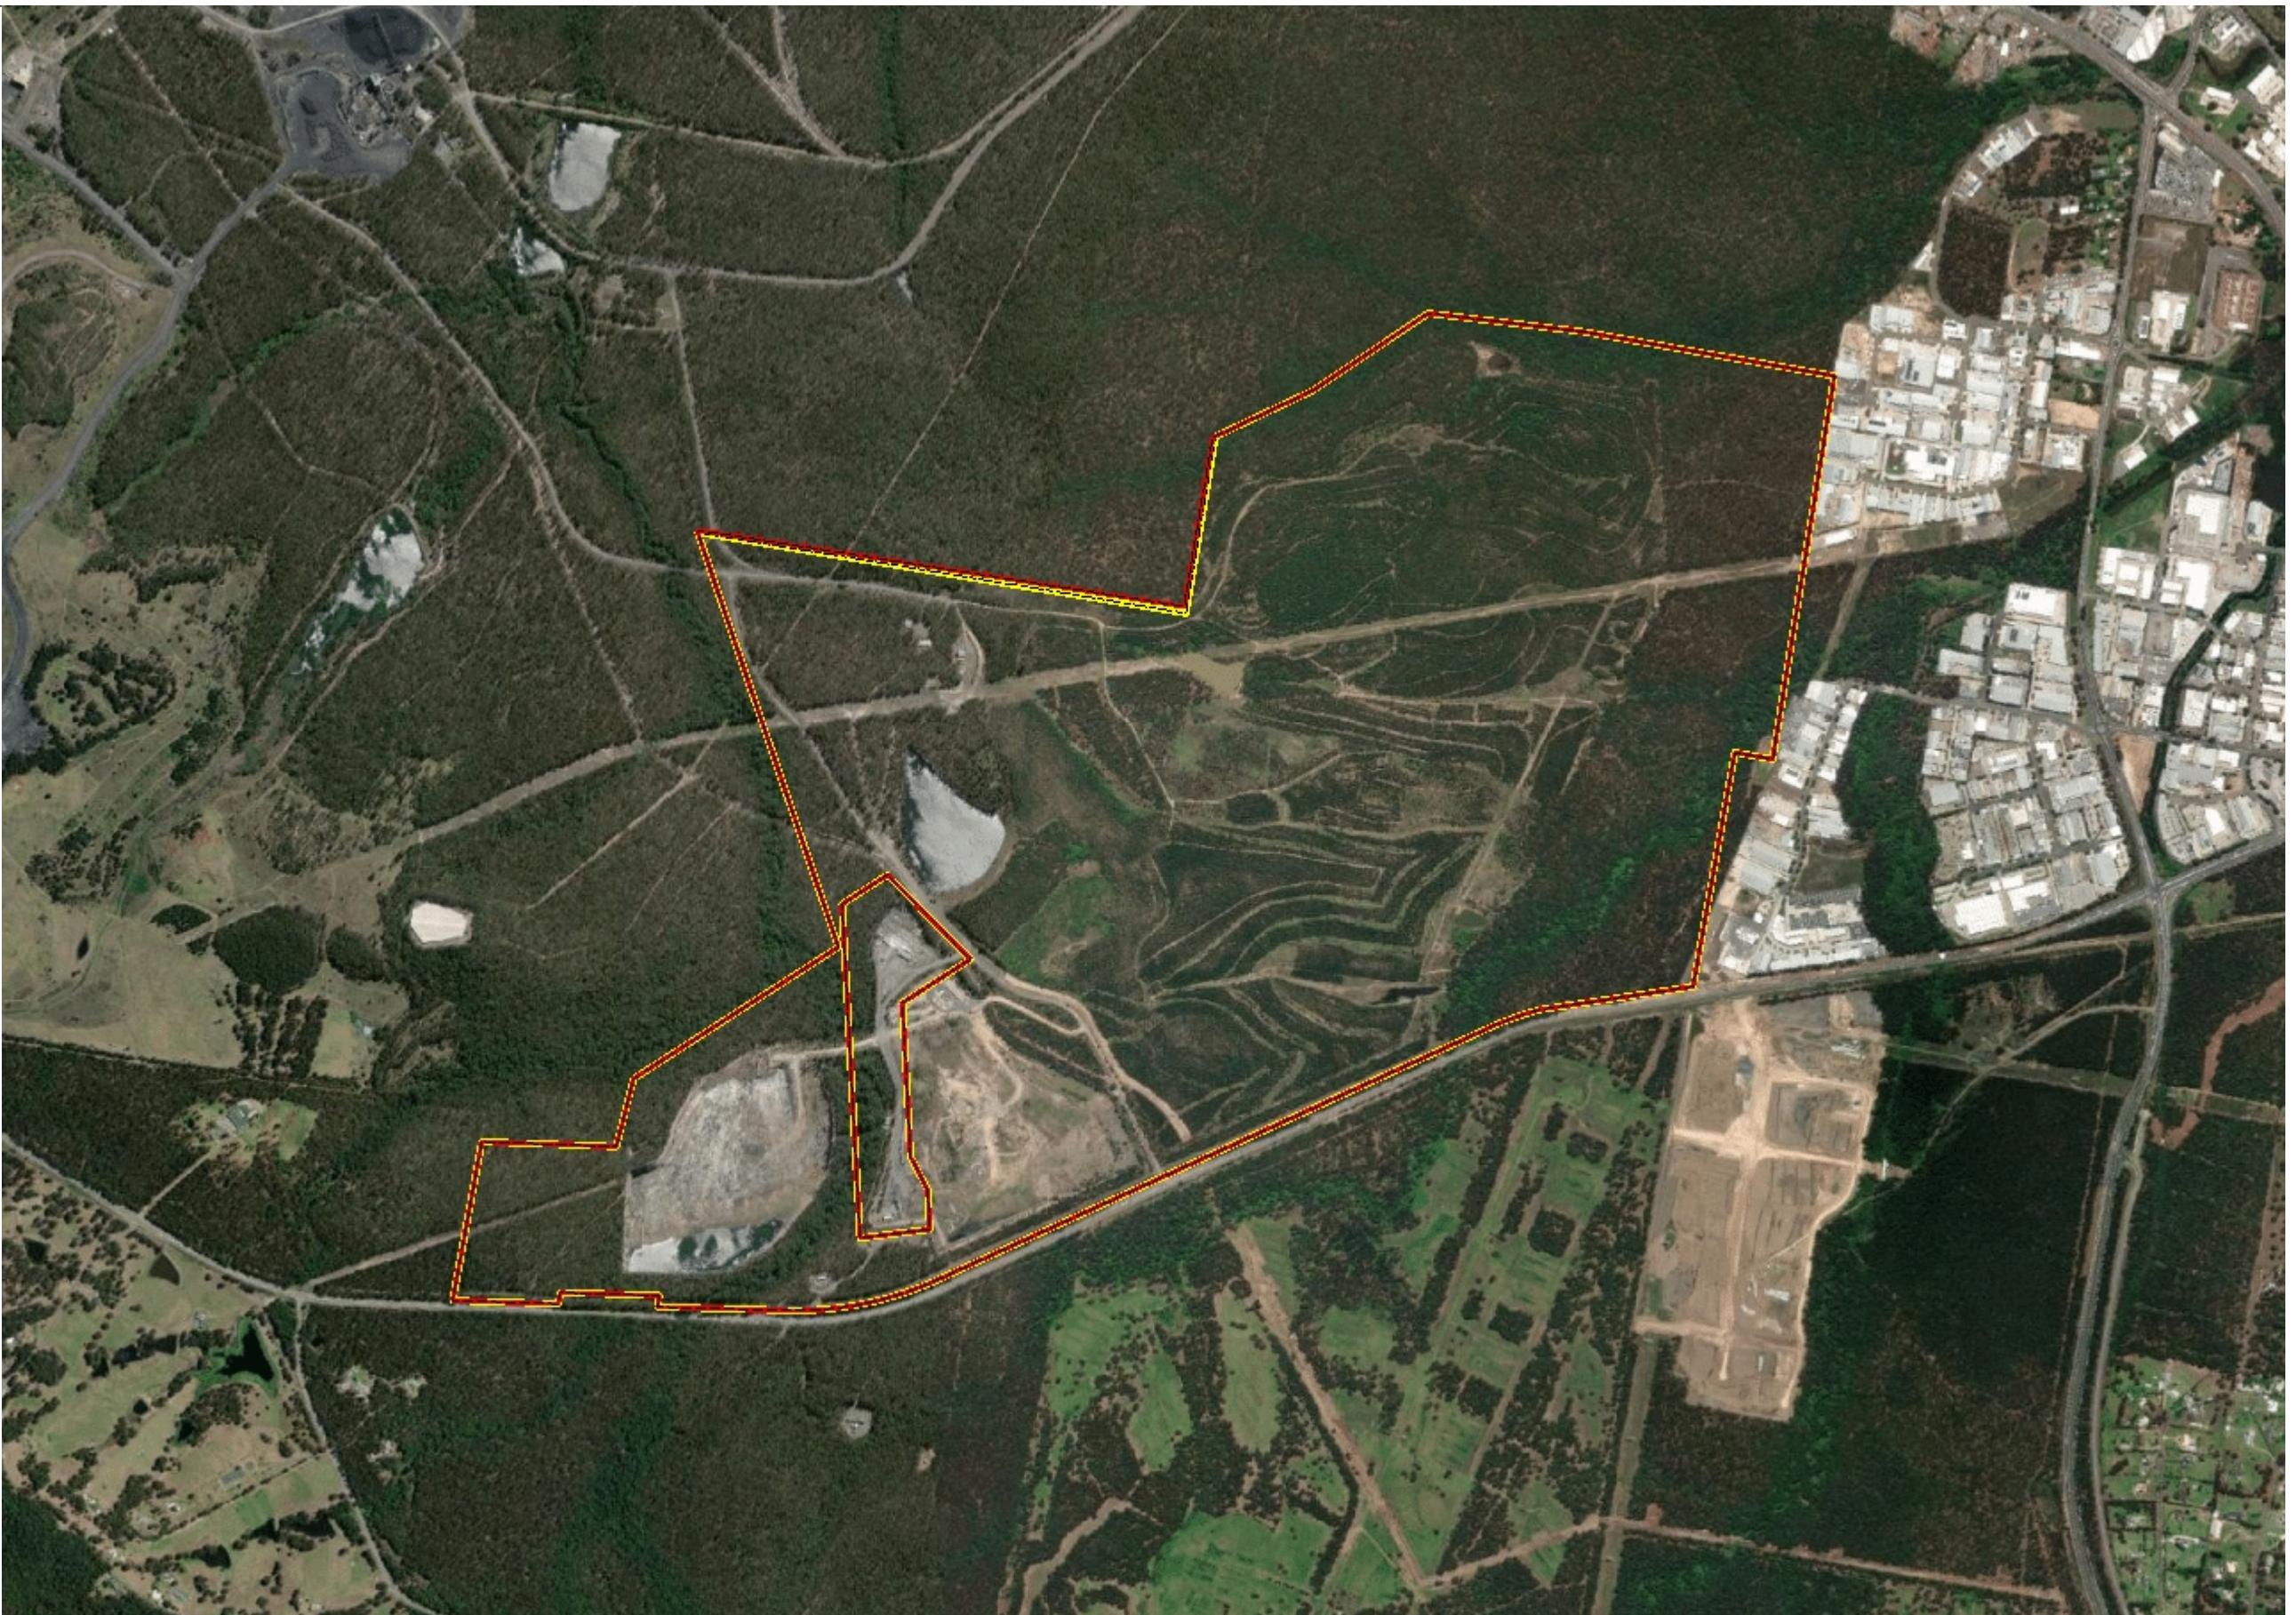

Legend

Forecast Data Year2

Forecast Disturbance

Forecast Land Prepared for Rehabilitation

Ecosystem and Land Use Establishment

Project Approval Boundary

Mine Operations Area

World Imagery

Low Resolution 15m Imagery

High Resolution 60cm Imagery

High Resolution 30cm Imagery

Citations

1,086.3 0 543.15 1,086.3 Meters

WGS_1984_Web_Mercator_Auxiliary_Sphere
© DRE


This map is a user generated static output from an Internet mapping site and is for reference only. Data layers that appear on this map may or may not be accurate, current, or otherwise reliable.

THIS MAP IS NOT TO BE USED FOR NAVIGATION

Notes

30/1/26
Submission ID number 11343

Donaldson Open Cut Coal Mine Plan 2C Mining and Rehabilitation – Year 3

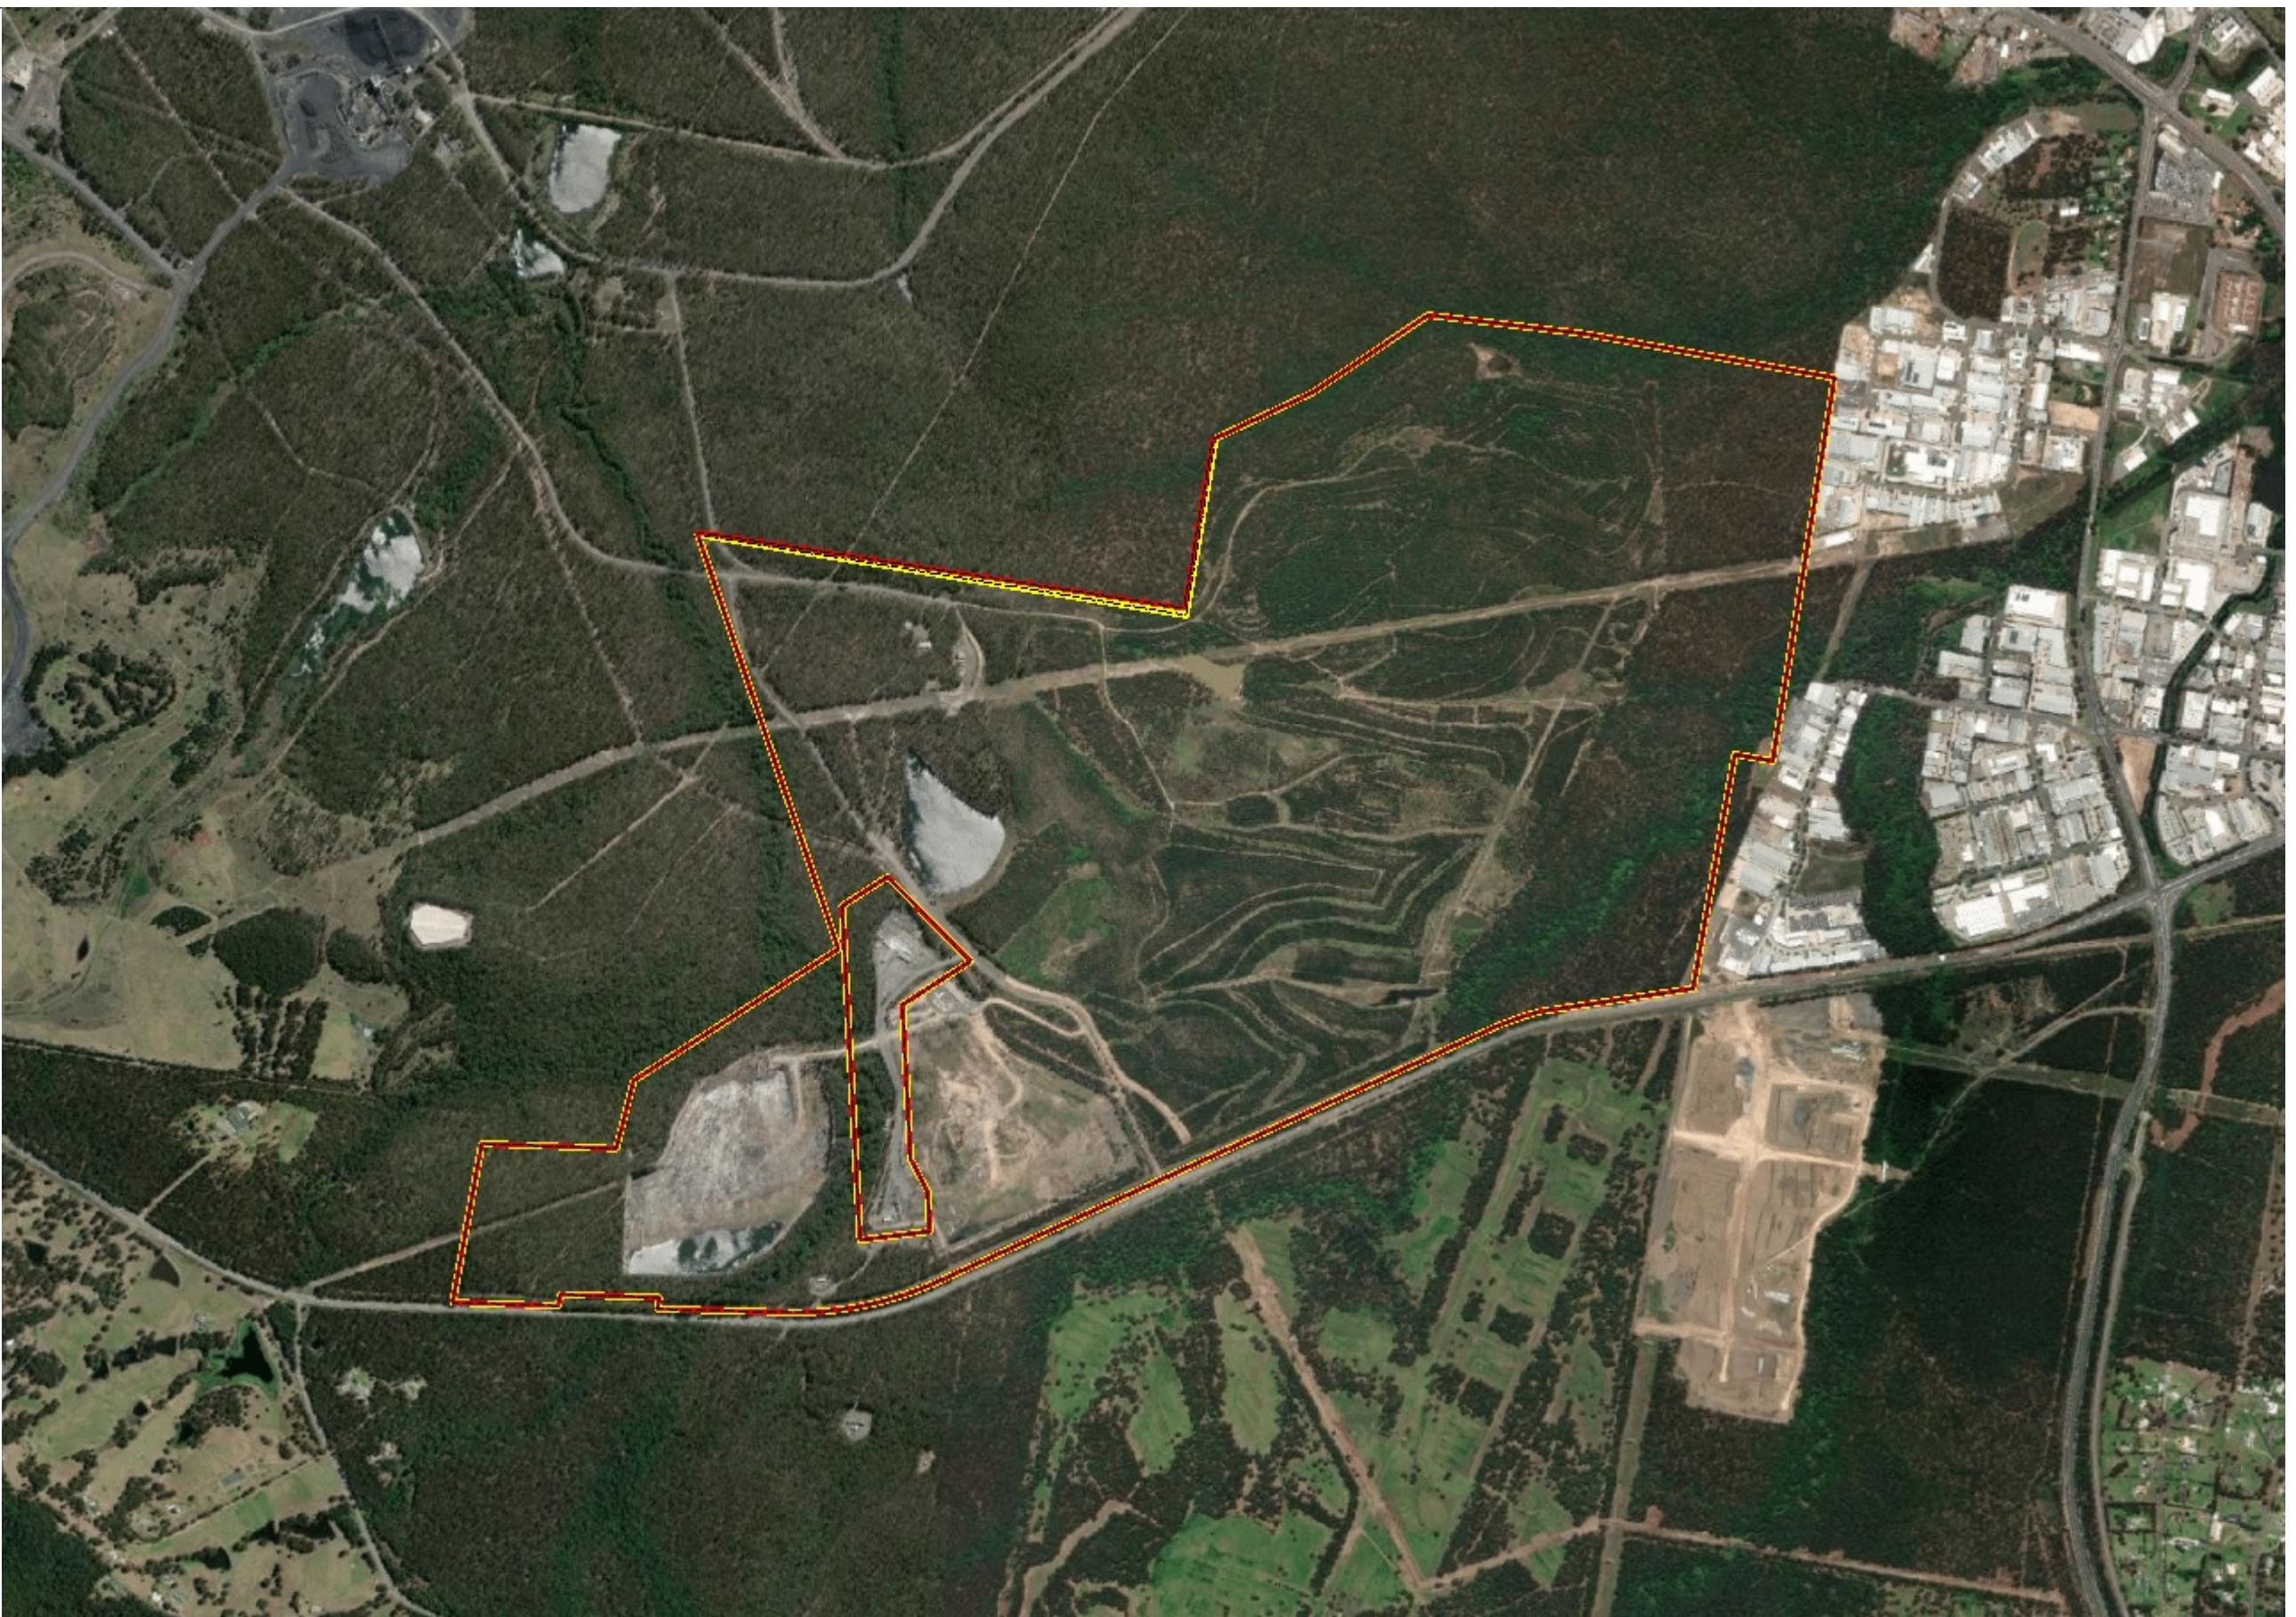

Legend

- Forecast Data Year3
 - Forecast Disturbance
 - Forecast Land Prepared for Rehabilitation
 - Ecosystem and Land Use Establishment
- Project Approval Boundary
- Mine Operations Area
- World Imagery
- Low Resolution 15m Imagery
- High Resolution 60cm Imagery
- High Resolution 30cm Imagery
- Citations

Notes

30/1/26
Submission ID number 11344

1,086.3 0 543.15 1,086.3 Meters

WGS_1984_Web_Mercator_Auxiliary_Sphere
© DRE

This map is a user generated static output from an Internet mapping site and is for reference only. Data layers that appear on this map may or may not be accurate, current, or otherwise reliable.

THIS MAP IS NOT TO BE USED FOR NAVIGATION
